



**St. Luke's Fellowship Hall  
Photo Update  
5/29/18**



**Exterior – Breezeway**  
Ceiling primed & painted



## Exterior – Youth Center Left Side

Cedar wood siding primed

Waiting for color decision





## Exterior – Youth Center Right

Cedar wood siding primed

Waiting for color decision



## Interior – Youth Center

Drywall patching & sanding in progress

All 2x6 beams installed

Remaining light fixture demo complete





## Interior – Youth Center Left

Ceiling grid installed  
Light Fixtures installed  
Grilles and duct work





## Interior – Youth Center Right

Ceiling grid installed  
Light Fixtures installed



## Interior – Youth Center

Drywall finishing & sanding in progress  
Floor scarified





## Game Room

Can lights installed

Grilles installed

Drywall finishing & sanding in progress



## Café

Can lights installed

Grilles installed

Drywall finishing & sanding in progress





## Exterior

Stucco replaced fresh air louvers

Trim added




**Security Lobby**  
Stucco complete  
PH Tested, not ready to paint yet





## Security Lobby

Trim added to match Youth Center

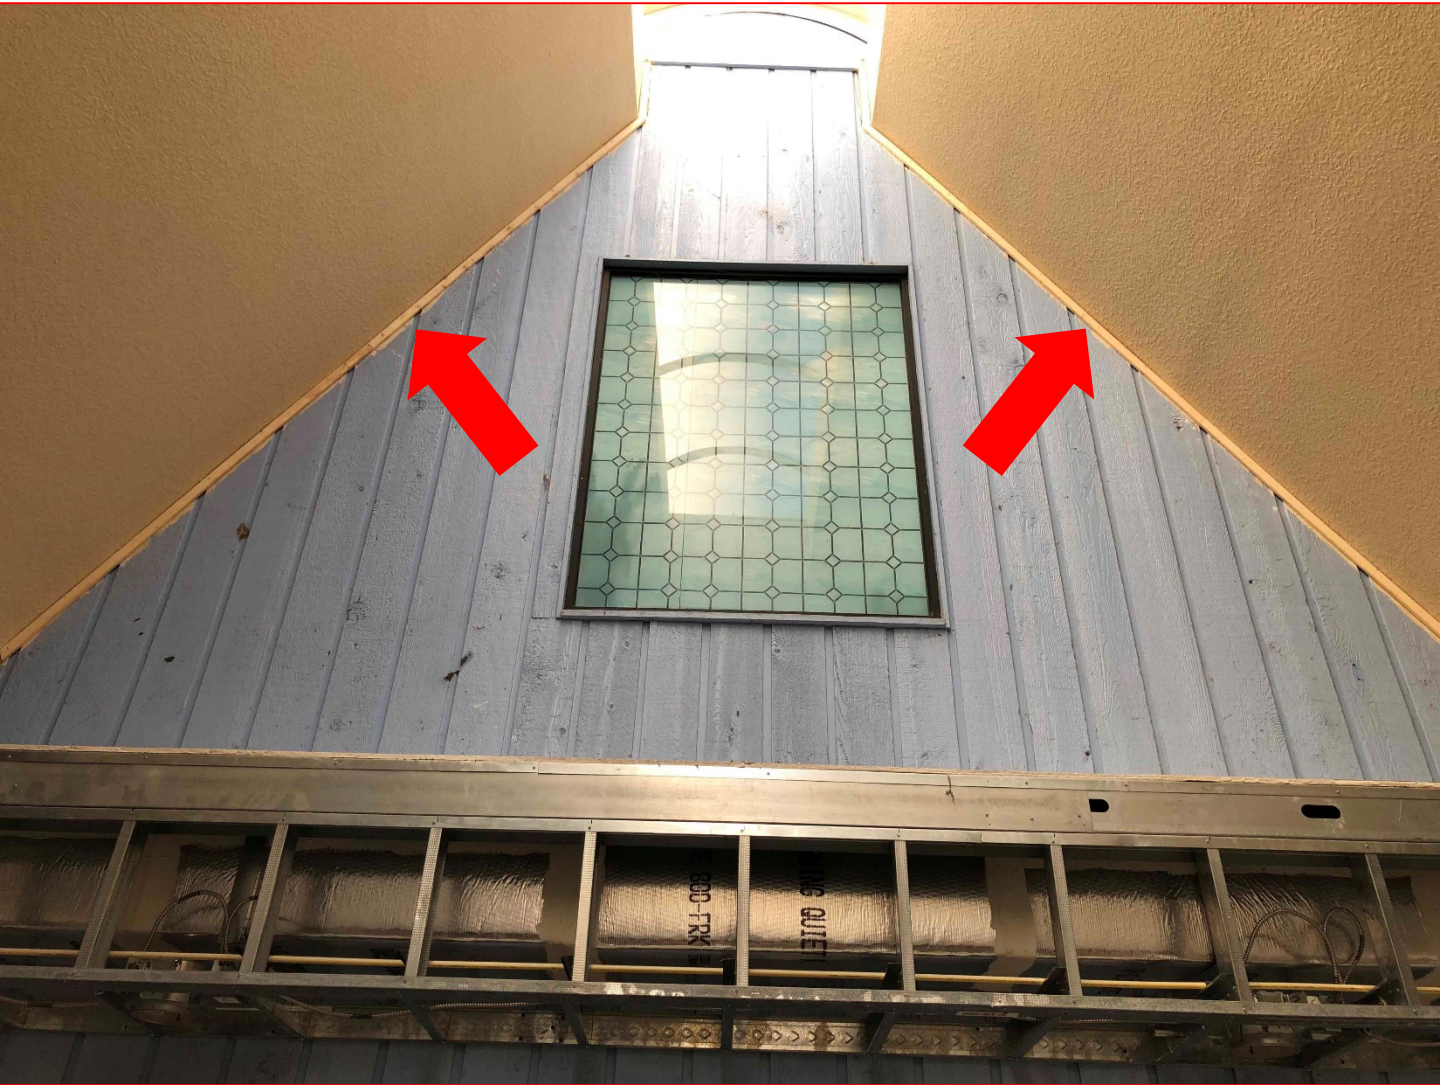

## **Week of 5/21/18:**

- Drywall
  - Finishing
  - Install final 2x6 for skylight shades
- HVAC
  - Duct work
  - Grilles
- Stucco
  - Finished stucco
- Electrical
  - Above ceiling work
  - Above Ceiling inspection for hard ceilings – PASSED 5/25
- Flooring
  - Demo & scarify
- Millwork
  - Field measure
  - Reviewed samples with Doug
- Windows
  - Field measure
- Paint
  - Primed Exterior Wood Siding
  - Painted Youth Center breezeway ceiling

## **Week of 5/28/18:**

- Drywall
  - Finishing & Sanding
- Concrete
  - AC area – Demo fence & remaining concrete
- Paint
  - Continue painting
- HVAC
  - Continue grilles
- Electrical
  - Lighting control panels – need to confirm with St. Luke's
